



Southern Sudan W.F.P. Roads Progress Report - December 2006

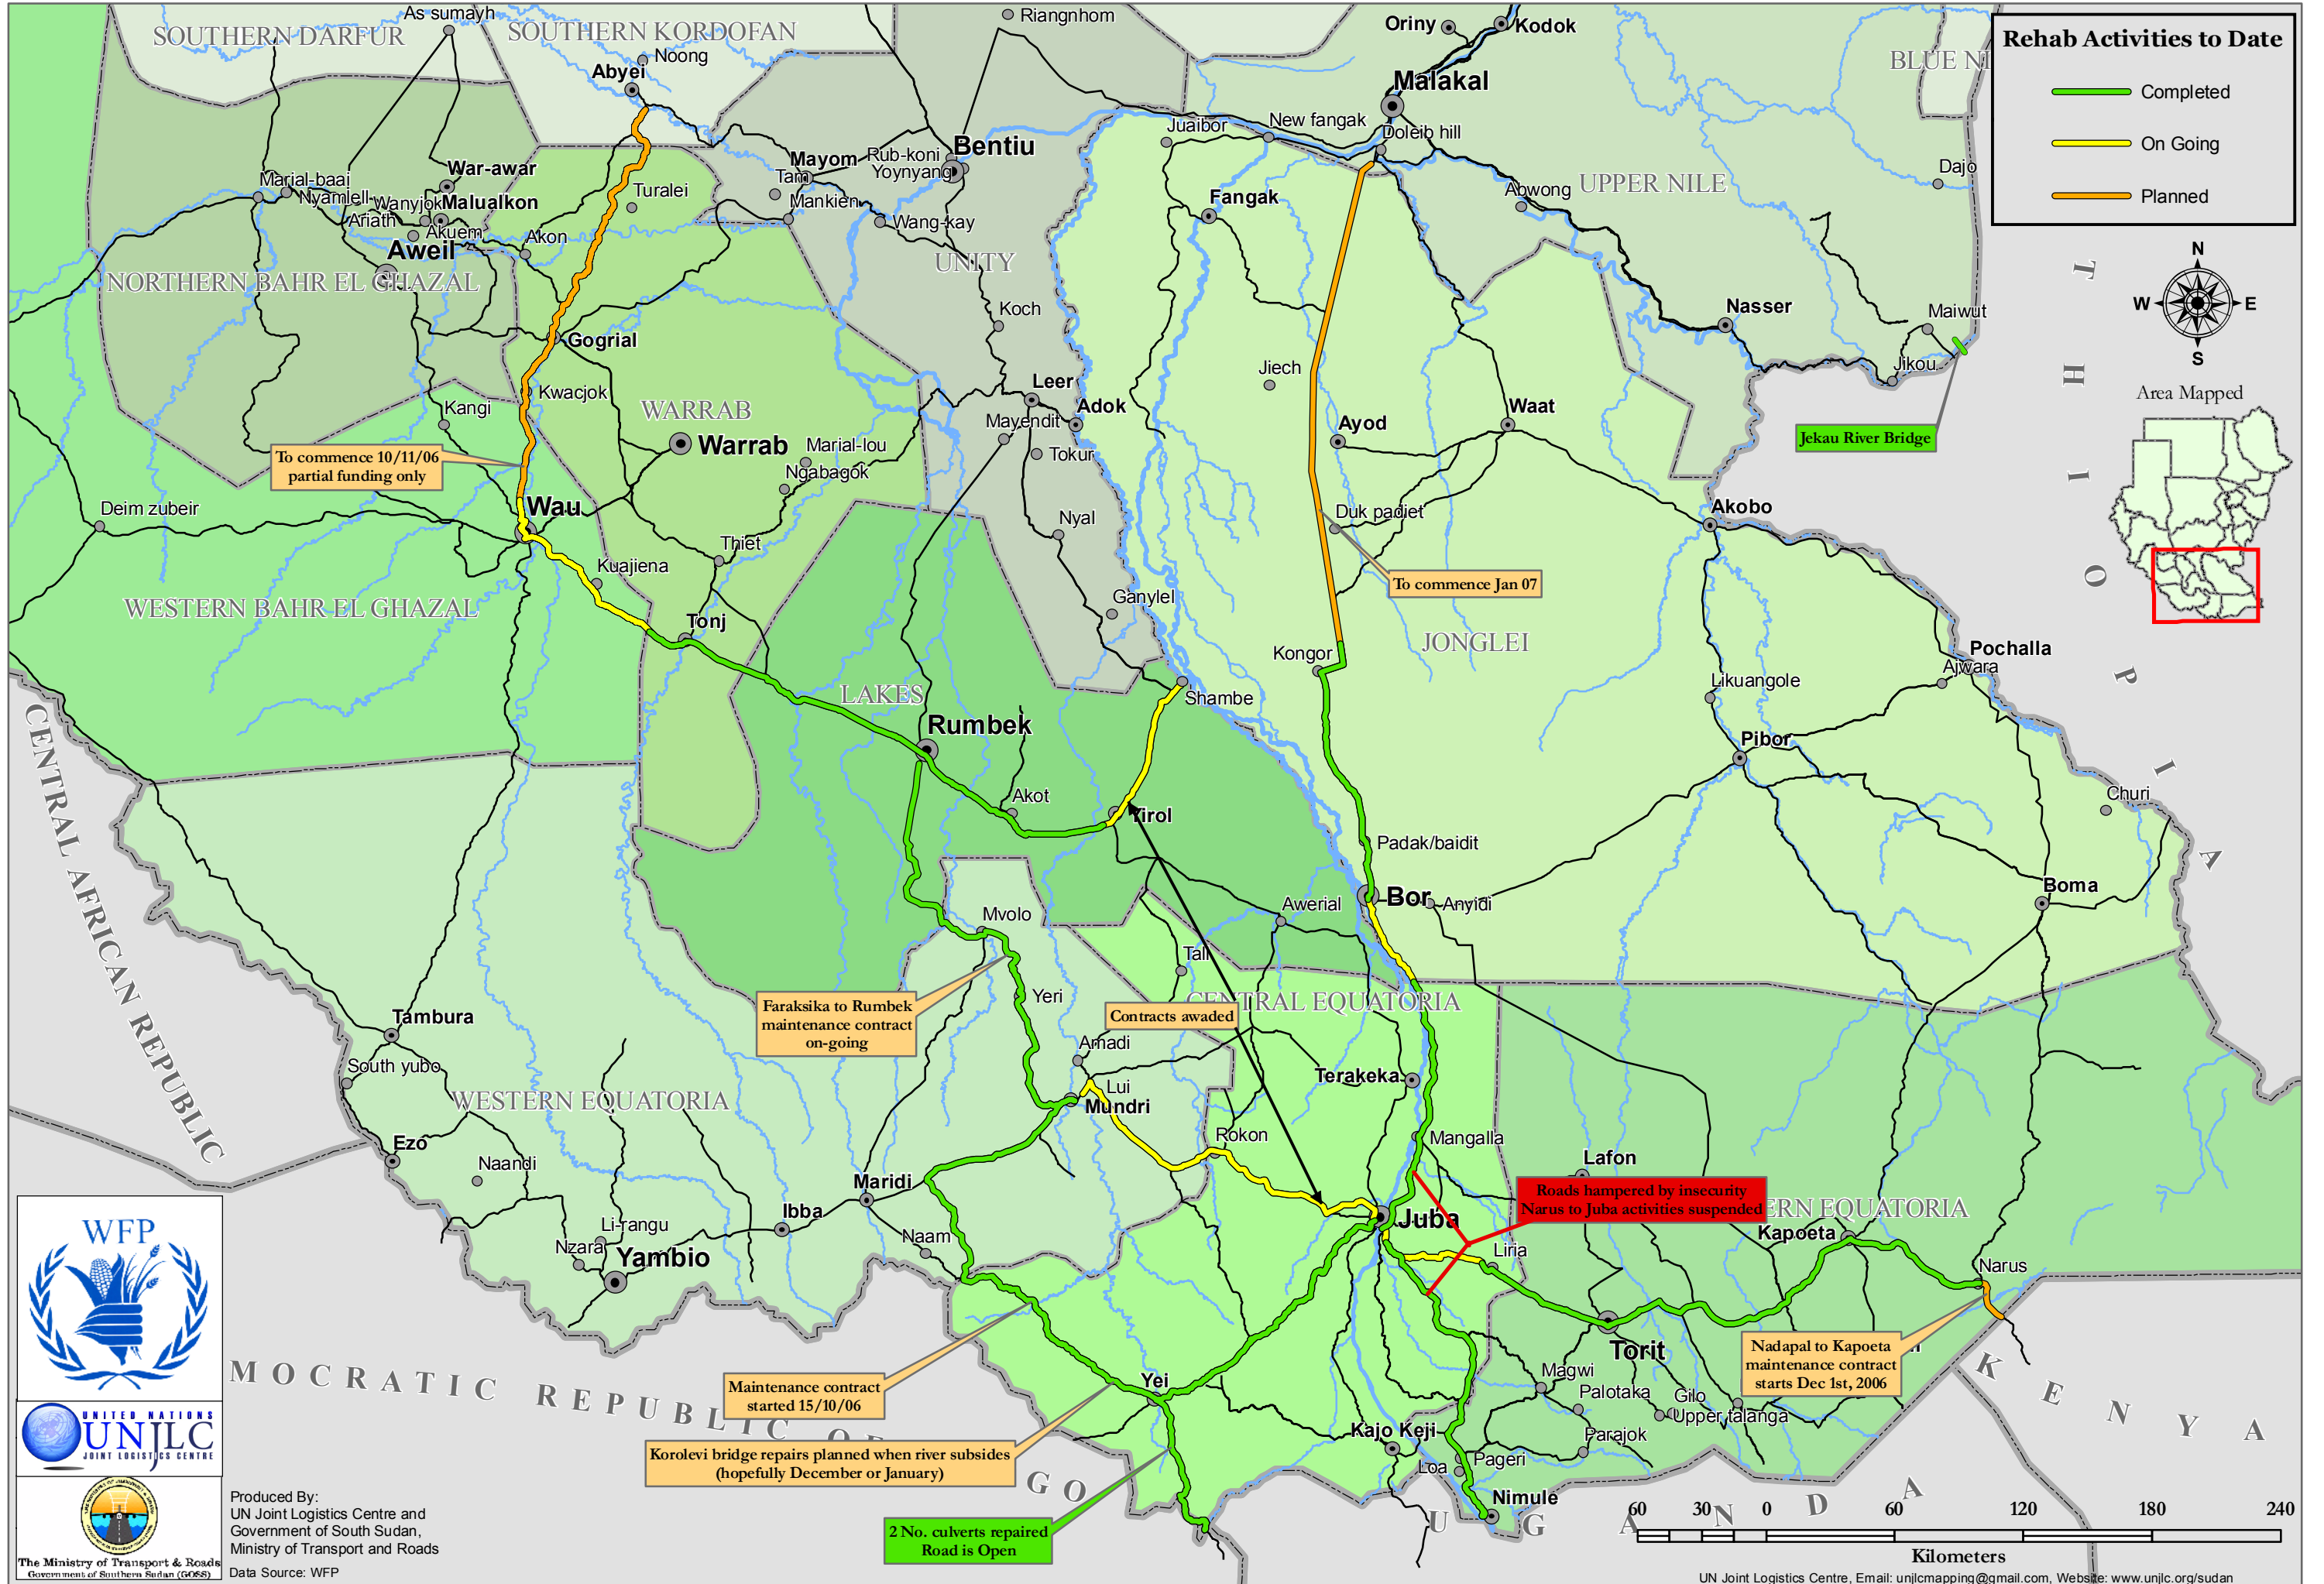

Rehab Activities to Date

- Completed
- On Going
- Planned



To commence 10/11/06
partial funding only

To commence Jan 07

Faraksika to Rumbek
maintenance contract
on-going

Contracts awarded


Roads hampered by insecurity
Narus to Juba activities suspended

Maintenance contract
started 15/10/06

Korolevi bridge repairs planned when river subsides
(hopefully December or January)

2 No. culverts repaired
Road is Open

Nadapal to Kapoeta
maintenance contract
starts Dec 1st, 2006



Produced By:
UN Joint Logistics Centre and
Government of South Sudan,
Ministry of Transport and Roads
Data Source: WFP
